FINAL PROJECT PROGRESS REPORT

The final progress report serves as a comprehensive written record of the progress and completion status of *"The Improving School Attendance in Rautahat District for Economically Disadvantaged Project (WE24NPL0010)"* in Madhesh Province, Nepal. This report provides an opportunity to present updates on the outcomes of the planned activities, along with the achievement of objectives and the utilization of the allocated budget.

Date (of Submission)	11 February 2025	**Report period:**	01/10/2024 to 7/02/2025

Submitted to:

Organization Full Name	Latter-Day-Saint Charities (LDSC)
Address	Krishna Bhawan,29-Narayan Gopal Marg, Batisputali Kathmandu-09, Nepal.
Contact Number	01-4110110,9704568862
Email Address	nepal.welfare2@churchservicemail.org

Implementing Organization Information

Organization's Legal Name	Madhesi Dalit NGO Federation (MDNF)
Address	Old Baneshowar,Prayag Marg, Bhimsengola Kathmandu-09,Nepal.
Contact Number	0097-01-4110094, 0097 9841 289 544
Email Address	info.mdnf@gmail.com, mdnfnepal_011@yahoo.com
Website	www.mdnfnepal.org

Contact Person for this Report

Prefix	Mr.
Full Name	Narendra Paswan
Title	Chairperson
Contact Number	+977 9841 289 544
Email Address	mdnfnepal_011@yahoo.com

Program/project information

Program/project title	The Improving School Attendance in Rautahat district for Economically Disadvantaged Project (WE24NPL0010) of Madhesh Province in Nepal.
Total grant amount (USD)	$33,304.30
Grant period	01/10/2024 to 15/06/2025 (9 Months)

Table of Contents

- Program/Project Description: 3
- Expected Outcomes: 3
- Project implementation Action Plan and Progress. 3
- Key Activities Accomplished 4
  - Pre-Approval Letter Sent: 4
  - Kik-off the project: 5
  - Education Materials Quotation Process and selection 5
  - Project Management Meeting: 6
  - Fund Release: 7
- Distribution Plan: 8
- Vehicle Rental for Field Visits and Airport Pickup/Drop 8
- Distribution of Educational Materials and Furniture Handover 9
- Program Overview: 9
- Media Coverage: 10
- Guest List: 10
- Images 12
- Cycle Distribution Program 14
- Program Overview: 14
- Cycle Distribution 15
- Cycle Beneficiaries Chart 15
- Guests and Participants 16
- Issues Faced During the Recent Bicycle Distribution 17
- Issue Faced in Student Data Collection 17
- Key Lessons Learned 20
- Conclusion: 22
- Summary Note of the Project 22

Program/Project Description

The project seeks to enhance the overall school environment by improving hygiene standards, learning facilities, and student well-being. By providing educational materials (such as bags and stationery), hygiene kits for both boys and girls, and bicycles to support their commute, the initiative aims to boost academic performance and reduce dropout rates. These efforts were being implemented at Shre Ram Naresh Laxman Secondary School, located in Rajdevi Municipality, Ward-02, Hajminiya, in the Rautahat district of Madhesh Province, Nepal.

Expected Outcomes:

a) **Increased Literacy Rates:** Improved educational resources and support will lead to higher literacy rates among students.
b) **Enhanced Learning Outcomes:** Students will benefit from a better learning environment, leading to improved academic performance.
c) **Improved Personal Hygiene:** Hygiene kits and better sanitary facilities will contribute to students' overall health and well-being.
d) **Increased Student Retention:** By addressing economic and resource-related barriers, the project aims to reduce dropout rates and increase student retention.
e) **Effective Teaching and Learning:** Enhanced infrastructure and resources will allow teachers to focus more on effective teaching and learning.

Project implementation Action Plan and Progress.

- ✓ Project Implementation Plan- 5 Months- 17th October,2024 -13rd March, 2025 (1st Kartik to 30 Falgun,2081)
- ✓ Project Vender Set-Up Change Form Signed Date: 26th September 2024, (10th Ashoj, 2081.)
- ✓ Project Agreement Signed Date: 28th September, 2024 (12th Asoj, 2081)

Key Activities Accomplished

Pre-Approval Letter Sent:

MDNF sent a formal request for pre-approval to Rajdevi Municipality and Sri Ram Naresh Laxman Secondary School, Hajminiya, Ward-02, Rautahat, Madhesh Province, on 29th September 2024. This step ensured that the concerned local authorities were informed about the project and provided their initial consent.

a) **MDNF Board Meeting Conducted:**

On 30th September 2024, MDNF organized a board meeting to discuss and finalize the project proposal before submitting it to the Social Welfare Council (SWC) for official approval.

b) **Approval from Rajdevi Municipality:**

The Rajdevi Municipality provided an official approval letter for the project on 2nd October 2024, confirming their support and permission for its implementation.

c) **Request Sent to SWC for Project Approval:**

After obtaining local approval, MDNF submitted a formal request to the Social Welfare Council (SWC) for final project authorization on 4th October 2024.

d) **Final Approval from SWC:**

On 7th October 2024, the Social Welfare Council officially approved the project, allowing MDNF to proceed with its implementation.

e) **MDNF Board Meeting for Project Planning (16th October 2024):**

A board meeting was held to share detailed project information, select staff, and establish the project management team. During the meeting, updates on progress were discussed, including the coordination efforts with Rajdevi Municipality and the school principal to collect accurate student data, review quotations, and identify the project's specific requirements.

f) **Project Implementation and Activities Launch (17th October 2024):**

The project officially commenced on this date, marking the beginning of planned activities.

g) **Information Sharing and Coordination (17th October 2024):**

MDNF sent formal letters to Rajdevi Municipality, the school, and other stakeholders to share information about the project and ensure coordination for its smooth implementation.

Note: These activities outline the step-by-step process of securing necessary approvals from local and national authorities to ensure smooth project execution. These steps highlight the structured approach to planning, collaboration, and the initiation of project activities.

Kik-off the project:

The project was officially launched on 1st Kartik 2081 at Sri Ram Naresh Laxman Secondary School, located in Hajminiya, Ward-02 of Rajdevi Municipality, Rautahat, Madhesh Province, Nepal. The District Project Coordinator, Mr. Shiv Shankar Paswan, took the lead in formally introducing the project to key stakeholders. He informed the school principal, Mr. Sanjay Kumar Yadav, about the project's objectives, scope, and planned activities.

Additionally, Mr. Paswan coordinated closely with the Chief Administrative Officer, Mr. Pralav Kayast, and the Mayor of Rajdevi Municipality, to ensure alignment with local authorities and secure their support for the project's successful implementation. These efforts were aimed at fostering collaboration and ensuring that the project could address the community's needs effectively while maintaining transparency and accountability.

Education Materials Quotation Process and selection

On 30th October 2024 (14th Kartik 2081), MDNF officially published a notice inviting quotations for the supply of educational materials and related items required for the project. This step ensured transparency and provided a fair opportunity for interested suppliers to participate. Suppliers were given 15 days to submit their proposals, with the final submission date set for 13th November 2024 (28th Kartik 2081).

A total of 14 supplier firms submitted their quotations for the project, which were divided between two offices: the Kathmandu Office and the Gaur Office in Rautahat. At the Kathmandu Office, six suppliers submitted their quotations, including three suppliers for bags and three for cycles. On the other hand, the Gaur Office in Rautahat received

quotations from eight suppliers. These included three suppliers for furniture, three for notebooks, one for hygiene kits, and one for health kits.

After carefully evaluating all the quotations based on key factors such as quality, cost, and suitability for the project, five supplier firms were selected. The chosen suppliers included one for furniture, one for cycles, one for bags, one for notebooks, and one each for hygiene and health kits. This selection process ensured that the suppliers chosen were well-equipped to meet the project's requirements while offering the best value in terms of quality and cost.

This process followed a transparent and competitive approach to ensure the selection of reliable suppliers for the required educational materials and resources. It contributed significantly to the project's readiness for implementation, aligning with its goals to improve learning environments and student well-being.

Project Management Meeting:

14 November 2024 (29th Kartik, 2081)

Location: Kathmandu Office

Attendees:

The Project Management team, consisting of five members from the MDNF Board and the Project Coordinator, attended the meeting to review the quotation selection process and finalize agreements. The participants included:

- Narendra Paswan
- Kumar Hazara
- Geeta Paswan
- Santoshi Bishwakarma
- Nitin Priyadarshi

Fund Release:

MDNF released funds to the office management on 17th October 2024 (1st Kartik, 2081), a Sunday, to initiate the procurement process. The funds were allocated for the purchase of educational materials required for the project.

The procurement process for educational materials was divided into two categories based on the budget. Small budget items were purchased from roster firms, while large budget items were acquired through firms that were selected based on their submitted quotations. Within 10 days of receiving the funds, all the required materials were successfully collected and stored. The procured items included a variety of educational resources such as benches, desks, cycles, school bags, notebooks, hygiene kits, and health kits, ensuring that the project was well-equipped to support the needs of the beneficiaries. The items procured include:

a) 100 sets of benches/desks

b) 80 cycles (45 for girls and 35 for boys)

c) 786 school bags

d) 3500 notebooks

e) 786 hygiene kits (Toothbrush, Toothpaste, Nail Clippers, Comb, Bandages)

f) Health kits for 127 girls (grades 7-10) (Sanitary Napkins, Bandages, Antiseptic Wipes, towel)

Material Storage:

There was ensured proper storage and management of the procured educational materials, MDNF secured a store in Gaur. The store was rented for a period of five days, from 7th to 11th Mansir, 2081 (22nd to 26th November, 2024), to accommodate and manage the educational materials.

Distribution Plan:

The plan is to distribute the educational materials on 10th Mansir, 2081 (25th November, 2024), ensuring that the items are delivered to the respective beneficiaries in a timely manner. The procurement, storage, and distribution process were the successfully collaboration between the project management team and the selected suppliers. All activities are on track for timely distribution.

Vehicle Rental for Field Visits and Airport Pickup/Drop

Kartik Month (November 2024) - 5 Days

1. **3rd November, 2024:** Murtuja Ansari traveled from Janakpur to Gaur for 1 day.
2. **5th-6th November, 2024:** Dhiraj Kumar Sah undertook local travel in Gaur-Rajdevi Municipality and visited schools for 2 days.
3. **10th-11th November, 2024:** Murtuja Ansari continued local travel within Gaur-Rajdevi Municipality for 2 days, focusing on school visits.

Mansir Month (November 2024) - 9 Days

1. **21st-25th November, 2024:** Dhiraj Kumar Sah visited Gaur-Rajdevi-School for local surveys and monitoring for 4 days.
2. **26th November, 2024:** Dhiraj Kumar Sah traveled from Gaur to Janakpur and back for a guest drop-off, covering 1 day.
3. **24th-26th November, 2024:** Murtuja Ansari traveled locally within Gaur, including meetings with the mayor and municipal officers, and visited the field office. The trip also included an airport drop-off at Simra, totaling 2 days.
4. **25th November, 2024:** Murtuja Ansari visited schools for the distribution of bags in Gaur, taking 1 day.
5. **26th November, 2024:** Murtuja Ansari provided a guest drop from Simra Airport to Kathmandu for 1 day.

Paush Month (December 2024 - January 2025) - 9 Days

1. **31st December, 2024 - 8th January, 2025:** Dhiraj Kumar Sah carried out local monitoring, surveys, and stakeholder meetings in Gaur-Rajdevi Municipality and schools, covering 5 days.

2. **5th-8th January, 2025:** Murtuja Ansari visited local schools, conducted home visits for cycle-selected boys and girls, and provided an airport pickup for Simra. This took 4 days.

Clarification: This rental arrangement, covering a total of 23 days, supported the transportation needs of key personnel for field visits, school surveys, stakeholder meetings, and guest pick-ups/drop-offs across multiple locations in Gaur, Janakpur, Simra, and other project-related sites.

Event Report- I

Distribution of Educational Materials and Furniture Handover

Ceremony

Date of Event:

2081/08/10 (25th November, 2024) – Monday

Venue:

The event took place in Rajdevi Municipality, Rautahat, with 25 distinguished guests, 150 local political leaders, education enthusiasts, teachers, social activists, media representatives, stakeholders, and 786 students in attendance.

Program Overview:

The program was jointly operated by Miss Kiran Kumari Paswan and Mr. Dev Kumar Paswan, with the welcome speech delivered by Mr. Uday Narayan Ram, District Chairperson of MDNF Rautahat. The distribution of educational materials and the handover of furniture to the school were the key highlights of the event. These included 786 school bags, 3500 notebooks, 786 hygiene kits, and health kits for 127 girls from grades 7-10. The program also featured the handover of 100 sets of benches and desks to the school principal.

The furniture handover was conducted by Mr. Bhikhari Prasad Yadav, Mayor of Rajdevi Municipality, along with Mr. Richard Nuffer, Country Director for Nepal of Latter-Day Saint Charities (LDSC), USA, and Mrs. Lori Nuffer. Their participation added great value to the program, highlighting the collaborative efforts between local authorities and international partners.

Media Coverage:

The event was widely covered by the media. It was broadcast live by RED TV of Rautahat, and social media platforms such as Facebook provided live telecasts. Local print media and FM radio stations also reported on the event, ensuring extensive coverage across the Rautahat district and the broader Madhesh Province. MDNF arranged for a cameraman to capture the event, with volunteer services managing the live telecast via social media.

Distribution of Materials:

The distribution of educational materials was managed by a team of key guests, including the Mayor, Deputy Mayor, Chief Administrative Officer, LDSC representatives, MDNF officials, school management members, and teachers. The materials distributed included:

- 786 school bags
- 3500 notebooks
- 786 hygiene kits
- Health kits for 127 girls from grades 7-10

The program was organized with a high level of cooperation between local and national leaders, ensuring smooth coordination and distribution of materials.

Guest List:

Several prominent guests attended the event, contributing to its success:

1. **Program Chairs:**
    - Sri Kamal Dev Hazara, MDNF District Advisor and Senior Citizen of Rajdevi Municipality
2. **Chief Guest:**
    - Sri Bhikhari Prasad Yadav, Mayor of Rajdevi Municipality, Rautahat
3. **Special Guests:**
    1. Sri Binay Lama, Treasurer of Social Welfare Council (SWC), Kathmandu
    2. Mr. Richard Nuffer, Country Director Nepal, Latter-Day Saint Charities (LDSC), USA
    3. Lori Nuffer, Country Director Nepal, Latter-Day Saint Charities (LDSC), USA
    4. Smt. Rajkumari Devi Sah, Deputy Mayor, Rajdevi Municipality, Rautahat

5. Mr. Pralav Kayast, Chief Administrative Officer, Rajdevi Municipality
6. Mr. Sanjay Kumar Yadav, Principal of Sri Ram Naresh Laxman Secondary School, Hajminiya, Rajdevi Municipality
7. Mr. Narendra Paswan, National Chairperson, Madheshi Dalit NGO Federation (MDNF)
8. Mr. Sanup Mahato, Chairperson of Ward-02, Hajminiya, Rajdevi Municipality
9. Mr. Satymarayan Mahato, Chairperson of RNLS School Management Committee, Hajminiya
10. Smt. Geeta Paswan, National Treasurer of MDNF and Chairperson of Dalit Development Committee (DDC), Gaur, Rautahat
11. Smt. Santoshi Bishwakarma, National Board Member of MDNF
12. Er. Nitin Priyadarshi, National Project Coordinator, MDNF
13. Mr. Uday Narayan Ram, District Chairperson of MDNF, Rautahat
14. Rajendra Paswan, District Advisor of MDNF and Treasurer of DDC, Gaur, Rautahat
15. Mr. Sandeep Rajwanshi, Board Member of Rajdevi Municipality and Ward-2
16. Mr. Suresh Pandit, Chairperson of Ward-5, Rajdevi Municipality
17. Jay Prakash Yadav, Managing Director, RED TV, Gaur, Rautahat
18. Pradip Kumar Das, Reporter, News Book Daily Paper, Rautahat

Conclusion:

The event was a significant milestone for the community, with active participation from various stakeholders, including local government officials, educational authorities, social activists, and media representatives. The successful distribution of educational materials and the handover of essential furniture and kits will greatly benefit the students and schools in Rajdevi Municipality. The collaborative efforts of all involved parties ensured the program's success, and the extensive media coverage provided visibility to the importance of such initiatives in promoting education and social development in the region. An attendance sheet for the program attached for reference in ***Annex-1***.

Images

Principal Mr. Sanjay Kumar Yadav and LDSC Country Director Lori Nuffer are distributing bags to the children.

Country Director Lori Nuffer, Santoshi Bishwakarma (National Board Member of MDNF), and Kiran Paswan are distributing bags and hygiene kits by visiting each classroom

Volunteers are packaging hygiene kits

Volunteers are packaging hygiene kits, while Geeta Paswan (National Treasurer of MDNF and Chairperson of the Dalit Development Committee, Gaur, Rautahat) and Santoshi Bishwakarma (National Board Member of MDNF) are assisting the volunteers in managing the packaging.

In the picture, Sri Bhikhari Prasad Yadav (Mayor of Rajdevi Municipality, Rautahat), Sri Binay Lama (Treasurer of the Social Welfare Council, Kathmandu), and Lori Nuffer (Country Director of Nepal, Latter-Day Saint Charities, USA) are seated while students perform a traditional cultural dance.

In the picture, Sri Bhikhari Prasad Yadav (Mayor of Rajdevi Municipality, Rautahat), and Lori Nuffer (Country Director of Nepal, Latter-Day Saint Charities, USA),while Mr. Narendra Paswan (National Chairperson of Madheshi Dalit NGO Federation) is inspecting the quality of benches.

Event Report-II

Cycle Distribution Program

Date of Event:

2081/09/24 (8th January, 2025) – Wednesday

Venue:

Rajdevi Municipality, Rautahat, with participation from local political leaders, education enthusiasts, teachers, social activists, media representatives, stakeholders, and 786 students. The program was attended by 25 distinguished guests and a large local community of 150 people.

Program Overview:

MDNF organized a Bi-Cycle Distribution Program to support students from economically disadvantaged backgrounds and those facing significant challenges in accessing regular education. From 16th to 23rd Paush, 2081 (31st December 2024 to 7th January 2025), a team from MDNF conducted a door-to-door visit to monitor the economic conditions of students in Rajdevi Municipality (wards 2, 3, 4, 5, and 6) and Gaur Municipality (ward 9). During this visit, survey forms were distributed to students from classes 5 to 10, focusing on attendance, caste, disability, economic background, and distance from school.

A total of 440 survey forms were collected, and a selection committee formed by MDNF, including school principals, and local authorities used these forms to identify 81 deserving students (45 girls, 35 boys, and 1 student with disable boy) who has been receive bicycles. These students were chosen based on criteria including regular school attendance, belonging to Dalit or economically disadvantaged families, and those from far areas from the school.

Cycle Distribution

The program was jointly managed by Miss Kiran Kumari Paswan and Mr. Dev Kumar Paswan. The welcome speech was delivered by Mr. Uday Narayan Ram, the District Chairperson of MDNF Rautahat. The distribution of the 81 bicycles (45 girls, 35 boys, and 1 disabled boy) was led by Mr. Bhikhari Prasad Yadav, Mayor of Rajdevi Municipality, and Smt. Rajkumari Devi Sah, Deputy Mayor of Rajdevi Municipality.

The event was extensively covered, with a live telecast by RED TV of Rautahat, social media streaming on Facebook, and coverage by local print media and FM radio stations across the Rautahat district in Madhesh Province. MDNF also arranged for a cameraman to shoot the event, which was shared live on social media as a volunteer service.

Cycle Beneficiaries Chart

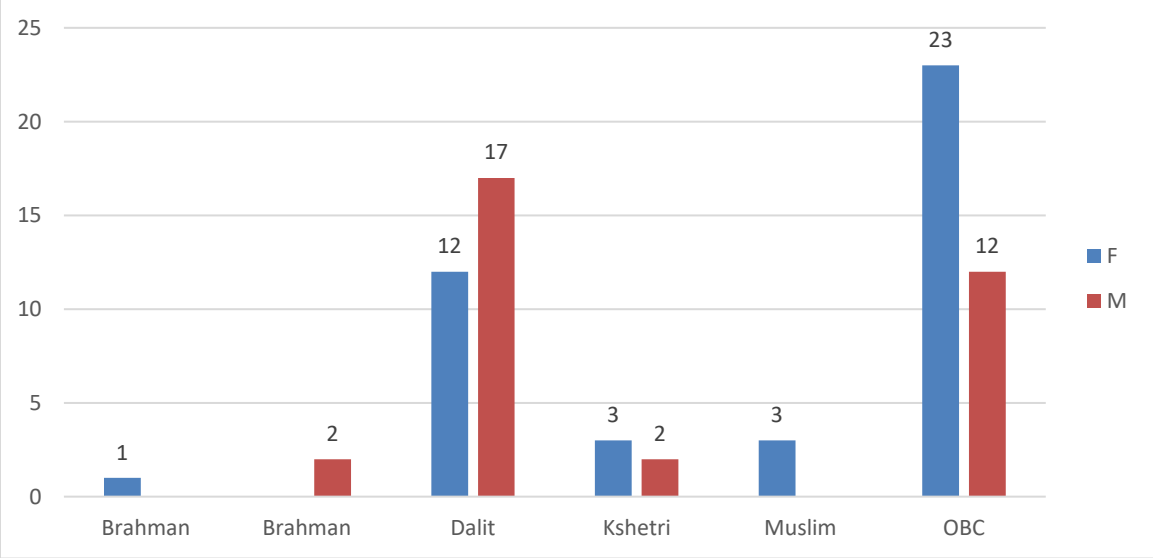

Count of Gender	**Column Labels**		
Row Labels	**F**	**M**	**Grand Total**
Brahman	1		1
Brahman		2	2
Dalit	12	17	29
Kshetri	3	2	5
Muslim	3		3
OBC	23	12	35
Grand Total	**42**	**33**	**75**

An additional 5 cycles have been reserved for distribution based on student performance.

Guests and Participants:

The event witnessed active participation from several important guests and dignitaries, including:

1. **Program Chairs:**
    1. Sri Kamal Dev Hazara, MDNF District Advisor and Social Activist from Rajdevi Municipality
2. **Chief Guest:**
    1. Sri Bhikhari Prasad Yadav, Mayor of Rajdevi Municipality, Rautahat
3. **Special Guests:**
    1. Smt. Rajkumari Devi Sah, Deputy Mayor, Rajdevi Municipality
    2. Mr. Pralav Kayast, Chief Administrative Officer, Rajdevi Municipality
    3. Mr. Sanjay Kumar Yadav, Principal of Sri Ram Naresh Laxman Secondary School, Hajminiya, Rajdevi Municipality
    4. Mr. Narendra Paswan, National Chairperson, Madheshi Dalit NGO Federation (MDNF)
4. **Guests:**
    1. Mr. Sanup Mahato, Chairperson of Ward-02, Hajminiya, Rajdevi Municipality
    2. Mr. Satymarayan Mahato, Chairperson of RNLS School Management Committee, Hajminiya
    3. Smt. Geeta Paswan, National Treasurer of MDNF and Chairperson of Dalit Development Committee (DDC), Gaur, Rautahat
    4. Smt. Santoshi Bishwakarma, National Board Member of MDNF
    5. Mr. Uday Narayan Ram, District Chairperson of MDNF, Rautahat
    6. Rajendra Paswan, District Advisor of MDNF and Treasurer of DDC, Gaur, Rautahat
    7. Mr. Sandeep Rajwanshi, Board Member of Rajdevi Municipality and Ward-2
    8. Mr. Suresh Pandit, Chairperson of Ward-5, Rajdevi Municipality

9. Jay Prakash Yadav, Managing Director, RED TV, Gaur, Rautahat
10. Pradip Kumar Das, Reporter, News Book Daily Paper, Rautahat

Issues Faced During the Recent Bicycle Distribution

During our recent bicycle distribution, we encountered unexpected challenges from the local government authorities of the area. We had conducted a thorough survey to identify students who genuinely needed bicycles based on factors such as their family's financial condition, distance from school (more than 10 km), and other relevant criteria. Based on this survey, we prepared a list of 80 deserving students.

However, just one day before the distribution, local authorities intervened, requesting to review the list of selected students. They then pressured us to remove some names and replace them with their children, relatives, and villagers, threatening to obstruct the distribution process if we did not comply. As a result, we had to allocate 15 bicycles according to their demands.

Following this, we lodged a formal complaint with the main police department. The issue was resolved with the intervention of higher authorities, allowing us to proceed with the distribution as planned and ensure that the bicycles were given to the deserving students.

Issue Faced in Student Data Collection

During our initial data collection from the school, we were provided with a student count of **663**. Based on this figure, we prepared the budget and planned the distribution of essentials accordingly. However, during a subsequent visit, we discovered a major miscalculation in the provided data. The school had inadvertently omitted two classes—**ECD (Early Childhood Development) and Grade 9**—from the total count. Upon correction, the actual number of students turned out to be **786**.

This miscalculation was a significant setback, requiring us to reassess and adjust our entire plan to ensure that no student was left out. Despite the challenges, we made the necessary changes and did our best to accommodate every student. Ultimately, we successfully provided essentials to all **786** students, ensuring that everyone received the support they needed.

Images

This moment marks the beginning of the cycle distribution event.

Sri Bhikhari Prasad Yadav (Mayor of Rajdevi Municipality, Rautahat), Mr. Sanjay Kumar Yadav (Principal), Mr. Narendra Paswan (Chairperson of Madheshi Dalit NGO Federation), Mr. Uday Narayan Ram (District Chairperson of MDNF, Rautahat), and Rajendra Paswan (District Advisor of MDNF and Treasurer of DDC, Gaur, Rautahat) attended the cycle distribution event and participated in distributing bicycles.

Mr. Sanjay Kumar Yadav (Principal), Mr. Narendra Paswan (Chairperson of Madheshi Dalit NGO Federation, distributing bicycles.

Key Lessons Learned:

a. **Effective Collaboration:** Seamless coordination between MDNF's central and district offices, volunteers, school officials, and local leaders contributed significantly to the project's success.

b. **Engagement with Local Communities**: Engaging local government and political leaders, teachers, social activists, and the community ensured broad support, increased participation, and heightened program visibility.

c. **Targeted Selection Process**: The approach of conducting surveys and monitoring attendance and socioeconomic conditions allowed for a more equitable and transparent selection of deserving students.

d. **Impact of Providing Basic Educational Resources**: Providing essential resources such as school bags, hygiene kits, health kits, and furniture created a positive and supportive learning environment for the students.

e. **Importance of Monitoring and Follow-up**: Regular home visits and data collection provided valuable insights into students' needs and helped ensure that the most vulnerable students received appropriate support.

f. **Media and Public Relations**: Using live telecasts, social media coverage, and local media outlets to publicize the event helped in amplifying the program's reach and impact.

g. **Logistical Planning and Execution**: Careful planning and coordination helped in the smooth distribution of bicycles and furniture, ensuring that resources reached students and schools effectively.

h. **Sustaining the Educational Impact**: Providing material resources was essential, but there is a need for ongoing support to ensure long-term academic success for students.

i. **Building Capacity for Future Initiatives**: Involving both staff and volunteers allowed for flexibility and efficiency in the execution of the program.

Recommendations:

a) **Enhance Collaboration with Local Stakeholders**: Future projects should continue fostering strong partnerships with local communities and stakeholders to ensure better coordination and participation.

b) **Expand Community Engagement**: Increasing community outreach and engagement activities will help to build long-term relationships, ensuring continued support for educational programs.

c) **Refine the Selection Process**: The selection process should be continuously evaluated and refined to ensure it is transparent and fair, helping to identify the most deserving students.

d) **Provide Additional Educational Tools**: Consider expanding the range of support offered, such as supplementary books, educational resources, and online learning tools, to further enrich the learning experience.

e) **Establish Ongoing Monitoring Mechanisms**: Implement a system for regular follow-up with the students who received support to track their progress and identify any additional needs they may have.

f) **Utilize Media for Long-Term Engagement**: Continue using a variety of media platforms to share the project's achievements, raise awareness, and engage potential partners and donors for future initiatives.

g) **Provide Continued Educational Support**: Future programs should focus not only on providing material resources but also on creating opportunities for ongoing educational development, such as scholarships or tutoring as well parents' awareness program.

h) **Invest in Capacity Building for Staff and Volunteers**: Provide ongoing training for staff and volunteers to ensure they are equipped to handle larger and more complex projects in the future.

Conclusion:

The Cycle Distribution Program was a significant event aimed at motivating and empowering students from economically disadvantaged families and encouraging regular school attendance. By providing these students with bicycles, MDNF has helped facilitate their access to education and promote their active participation in school activities. The event was a success, with active participation from local authorities, educational stakeholders, and the community leaders and members. The media coverage ensured that the impact of the program was widely acknowledged and appreciated. An attendance sheet from the program attached for reference in ***Annex-2.***

Summary Note of the Project

The Madheshi Dalit NGO Federation (MDNF) successfully implemented a project aimed at empowering students, especially those from economically disadvantaged backgrounds, by providing them with essential educational materials and support. The project was executed with the support of a dedicated team of 5 staff members and 8 volunteers, including personnel from both the central office and the district office in Gaur, Rautahat. The key members involved in the project were:

- Mr. Sanjay Kumar Pasee, Executive Director
- Er. Nitin Priyadarshi,Project Coordinator
- Mr. Suryadeep Kumar Gupta, Admin & Finance Officer
- Mr. Shiv Shankar Paswan, District Project Coordinator
- Mr. Rohit Kumar Paswan, Social Mobilizer

Together, this team worked tirelessly to ensure the successful distribution of educational materials and resources to the students in the target schools. The project focused on several key interventions to support students' education and well-being:

a. School Bags and Hygiene Kits: A total of 786 students received school bags and hygiene kits, helping to improve their daily school life and hygiene practices.

b. Health Kits for Girls: 127 girls from grades 7 to 10 received health kits, addressing their health needs and promoting well-being.
c. Cycles for Deserving Students: 81 deserving students, including 45 girls and 35 boys, along with one disabled boy, were selected to receive bicycles. This initiative aimed to facilitate their regular attendance at school, especially for those who faced long distances or other barriers to accessing education.
d. Furniture Handover: 100 sets of benches and desks were handed over to the schools, providing students with a comfortable and conducive learning environment, enabling them to sit and study freely without distraction.

The overarching goal of the project was to empower students and raise awareness among them and their parents about the importance of regular school attendance and its long-term benefits. By providing the necessary materials and a better learning environment, the project contributed to improving the quality of education and fostering an atmosphere of growth and opportunity for students.

This initiative was not just about distributing items but also about making a lasting change in the community. It emphasized the transformative power of education and its role in shaping a better future. Education, often seen as the "light of the lamp," has the ability to dispel the darkness of ignorance and pave the way for brighter futures. Through this project, MDNF is making significant strides in improving society by fostering a culture of education, empowerment, and positive change.

The technical support provided by the Executive Director, Mr. Sanjay Kumar Pasi, and the collective effort of the entire team were pivotal in the success of this project. MDNF thanks all the volunteers, participants, and stakeholders who contributed to making this initiative a reality. Together, we are building a better and more educated future for the children of our community.

Annex-1 Attendance sheet of event one program.

मधेशी दलित गैर सरकारी संस्था महासंघ

Madheshi Dalit NGO Federation (MDNF)

Head Office: Old Baneshawar,Prayag Marg,Bhimsengola,Kathmandu

Branch Office: Gaur, Rautahat, Madhesh Province,Nepal

Education Meterials(Fruniture-Bench/Desk,School Bags,Notebooks,Hygiene Kits and Health kits) Distribution Program

Project: The Improving School Attendance in Rautahat for Economically Disadvantaged Project(WE24NPL0010)

Supporting Agency: Latter-Day Saint Chairities(LDSC), USA

Local Level & District: Rajdevi Municipality,Ward-02,Hajminiya,Rautahat

School Name: Sri Ram Naresh laxman Secondry School,Rajdevi-02,Hajminiya

Province: Madhesh Province **Participator's Attendance Sheet-2024** **Date:** 25 November,2024(10th Mansir,2081)

S N	Name of Participates	Organization/Address	Post	Gender	Age	Contact Number	Signature
1.	Bhikhari Pd. yadav -	Rajdevi Municipality	Mayer.	M			
2.	Raj Kumari Devi Sah	"	Dep. "	F			
3.	Bimaya Lama	SWC, Nepal	Treas - SWC	M			
4.	Lori Nuffer	LDSC/ KTM		F			Lori Nuffer
5	Richard Nuffer	LDSC/KTM		M			
6	Kamal Dev Hazari	Rajdevi pahari		M			
7	Sanup Mahato	Rajdevi-2 Hajminiya		M			
8	Suresh pandit	" 5 Hajminiya		M			
9	Rajhar Nandan Singh	" 5 "		M			
10	Hemendra prasad yadav	" 7	H.M	M			
11	Ramdaribo sahani	Rajdevi 5	H.M.	M		9845376145	
12	Santosh Bishwakarma	Kathmandu	BORD. member	F		9842448055	
13.	Geeta Paswan	MDNF/DDC	Treasurer	F	40	9845642348	Geeta
14	Rajendra Paswan	Gaur-2			77	9845384816	
15	Sheikh Mazbar Alam	Gaur-9				9851007921	Mazbar
16	Binod Kushwaha	Jagdish primary School Hajminiya	Teacher	M		9845041284	
17	Yogendra Baitha	Hajminiya-2		M			
18.	Sandeep Rajvanshi	" Bord member	M. P. Bord member	M		9884058311	
19	Suman Mahato						
20	Ram kumar singh -						
21	Rajendra Baitha			M		9845663919	
22	Amrendra ku Singh			M		9845134911	
23	Manoj Kumar Singh	RNL School Hajminiya	Science Teacher	M		9845162649	Manoj
24	Babulal Paswan	" "	Teacher	M		9845798336	
25	Saiban Nesta	Bisanpur member	Bord member	F			
26	Suchita Shrivastav	Gaur-9	Teacher	F		9845719097	
27	Vijay Kishor Shrivastav	Rajdevi-2	Teacher	M.		9845122251	
28	Renita Kumari Karn	Gaur-4	Teacher	F		9844031964	
29	Onita yadav.	Rajdevi-1	Teacher	F		9845387522	Onita
30	Jyoti Kumari Singh	Gaur-5	Teacher	f		9844540225	
31	Anju Devi	Hajminiya-5	Teacher	f		9841238484	

13.	Geeta Paswan	MDNF/DDC	Teacher/ch	F	40	9845643348	Geeta
14	Rajendra Paswan	Gaur-2			77	9845338486	
15	Sheikh Manzoor Alam	Gaur-9				9851007921	Manzoor
16	Binod Kushwaha	Jagdish primary school Hajminiya	Teacher	M		9845041284	
17	Yogendra Baitha	Hajminiya-2		M			
18.	Sandeep Rajvanshi	" Bord member	M.P. Bord member	M		9884059311	
19	Sukhdev Prasad						
20	Ram pukar singh –						
21	Rajendra Baitha			M		9845663914	
22	Amrendra ku. Singh			M		9845134911	
23	Manoj Kumar Singh	RNT School Hajminiya	Science Teacher	M		9845162649	Manoj
24	Babulal. Paswan	" "	Teacher	M		9845798296	
25	Saiban Nesha	Bibi member	Bord member	F			
26	Suchita Shrivastav	Gaur-9	Teacher	F		9845719097	
27	Vijay Kishor Shrestha	Rajdevi-2	Teacher	M.		9845122251	
28	Ranita Kumari Karn	Gaur-4	Teacher	F		9844031964	
29	Anita yadav.	Rajdevi-1	Teacher	F		9845387522	Anita
30	Jyoti Kumari Singh	Gaur-5	Teacher	f		9844540225	Jyoti
26	Anju Devi	Hajminiya-5	Teacher	f		9841233486	

46	Narendra Paswan	MDNF	National Chairperson	M	49	9841289544	Narendra
47	Kiran Paswan	MDNF	Bord member	F	38	9845138691	
48							
49							
50							
51							
52							
53							
54							

Annex-2 Attendance sheet of event two program.

मधेशी दलित गैर सरकारी सँस्था महासँघ

Madheshi Dalit NGO Federation (MDNF)

Head Office: Old Baneshawar,Prayag Marg,Bhimsengola,Kathmandu

Branch Office: Gaur, Rautahat, Madhesh Province,Nepal

Education Meterials(Fruniture-Bench/Desk,School Bags,Notebooks,Hygiene Kits and Health kits) Distribution Program

Project: The Improving School Attendance in Rautahat for Economically Disadvantaged Project(WE24NPL0010)

Supporting Agency: Latter-Day Saint Chairities(LDSC), USA

Local Level & District: Rajdevi Municipality,Ward-02,Hajminiya,Rautahat

School Name: Sri Ram Naresh laxman Secondry School,Rajdevi-02,Hajminiya

Cycle -81 Pcs(35- Boys /45 Girls and 1 Disable) Distribution Program

Province: Madhesh Province **Participator's Attendance Sheet-2025** **Date:** 8 January,2025(24th Paush,2081)

S N	Name of Participates	Organization/Address	Post	Gender	Age	Contact Number	Signature
1	Bhikhari Prasad yadav	Rajdevi Nemki Palika	Mayer-Chief guest	M	65		
2	Rajkumari Devi	,,	Deupty Mayer	F	50		
3	Kamal Dev Hazara	MDNF/Rautahat Advisor	Program Chairperson	M	65		Kamal Dev
4	Narendra Paswan	[illegible]	[illegible]	M	49		
5	Sanjay kumar yadav	Shree Ram Naresh Laxman Ser. School	Principal	M	38		
6	Rajendra paswan			M	68		Rajendra
7	Sanup mahato		Ward-2 chairperson	M	60		SHUP
8	Babulal paswan	Rajdevi-2 Hajamhiya	Teacher	M	52		
9	Raj Kumar sah			M			
10	Sandip man Raj Banshi	Rajedevi-2	Municipality Board member	M			
11	Satya Narayan mahto	Rajedevi-2	School management chairman	M			
12	[illegible] सिंह	Rajedevi-5					
13	Keshav Nandan Singh	Rajdevi-5					
14	Ram Pukar Singh	,,					
15	Hari Narayan yadav	Rajdevi-2					
16	Shyam yadav	,, ,,					
17	Uttee chandra Raj yadav	Rajdevi-1	School Principal-Pocha	M			
18	Shiv Shankar paswan	Gaur-9	Social Activist	M	38		
19	Bindeshwar Mahato	Rajdevi-2	,,	M			
20	Ram Prabesh mahto	,,		M			
21	Raja Ram Singh	Rajdevi-5		M			

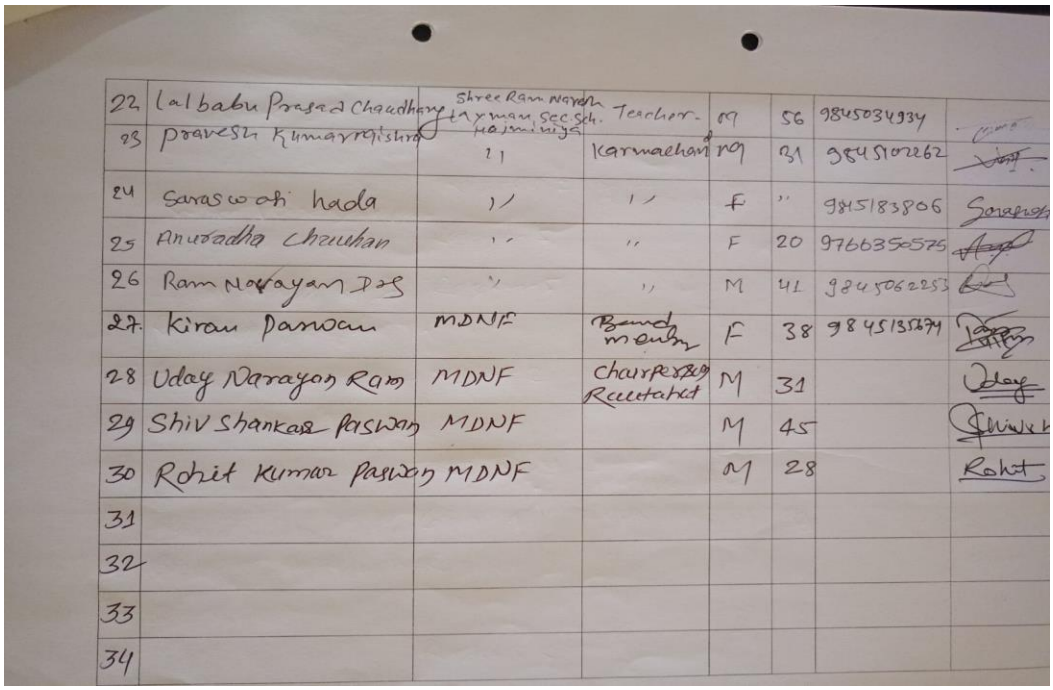

22	Lalbabu Prasad Chaudhary	Shree Ram Narayan Laxman Sec. Sch. Hasminiya	Teacher	M	56	9845034934	
23	Pravesh Kumar Mishra	"	Karmachari	M	31	9845102262	
24	Saraswati Yada	"	"	F	"	9835183806	
25	Anuradha Chauhan	"	"	F	20	9766350575	
26	Ram Narayan Das	"	"	M	41	9845062253	
27.	Kiran Panwar	MDNF	Board member	F	38	9845131274	
28	Uday Narayan Ram	MDNF	Chairperson Rautahat	M	31		
29	Shiv Shankar Paswan	MDNF		M	45		
30	Rohit Kumar Paswan	MDNF		M	28		Rohit
31							
32							
33							
34							

The End
